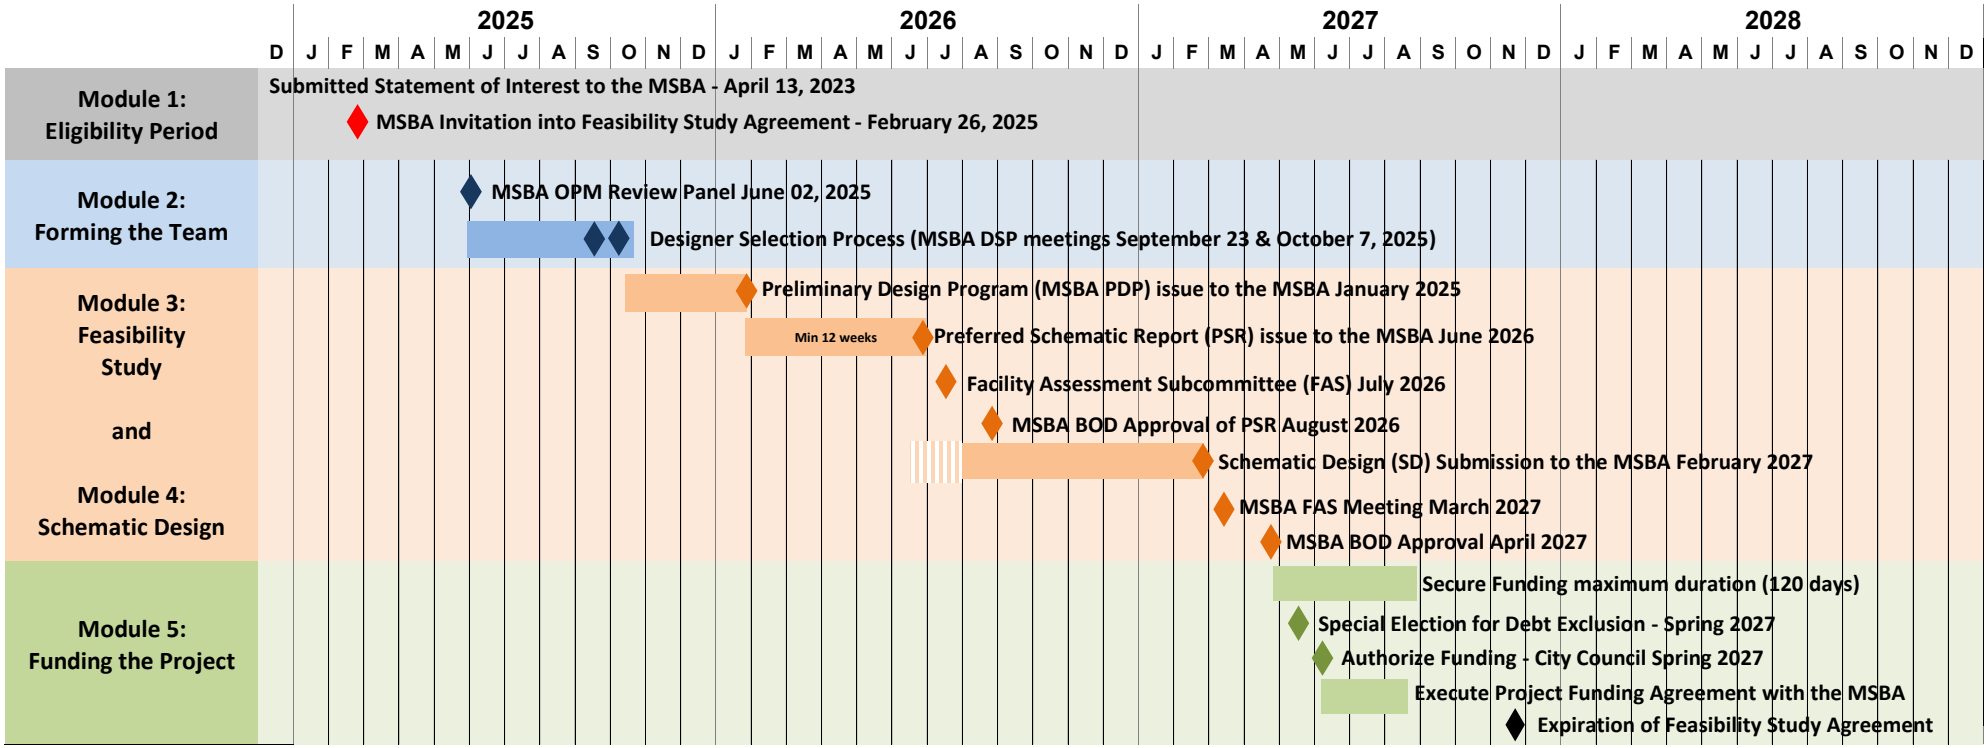
2025
2026
2027
2028
D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D
Module 1: Eligibility Period
Submitted Statement of Interest to the MSBA - April 13, 2023
MSBA Invitation into Feasibility Study Agreement - February 26, 2025
Module 2: Forming the Team
MSBA OPM Review Panel June 02, 2025
Designer Selection Process (MSBA DSP meetings September 23 & October 7, 2025)
Module 3: Feasibility Study
and
Module 4: Schematic Design
Preliminary Design Program (MSBA PDP) issue to the MSBA January 2025
Min 12 weeks
Preferred Schematic Report (PSR) issue to the MSBA June 2026
Facility Assessment Subcommittee (FAS) July 2026
MSBA BOD Approval of PSR August 2026
Schematic Design (SD) Submission to the MSBA February 2027
MSBA FAS Meeting March 2027
MSBA BOD Approval April 2027
Module 5: Funding the Project
Secure Funding maximum duration (120 days)
Special Election for Debt Exclusion - Spring 2027
Authorize Funding - City Council Spring 2027
Execute Project Funding Agreement with the MSBA
Expiration of Feasibility Study Agreement
